




U.S. Route 24

Realignment/Expansion from
Fort Wayne, Indiana to
Toledo, Ohio

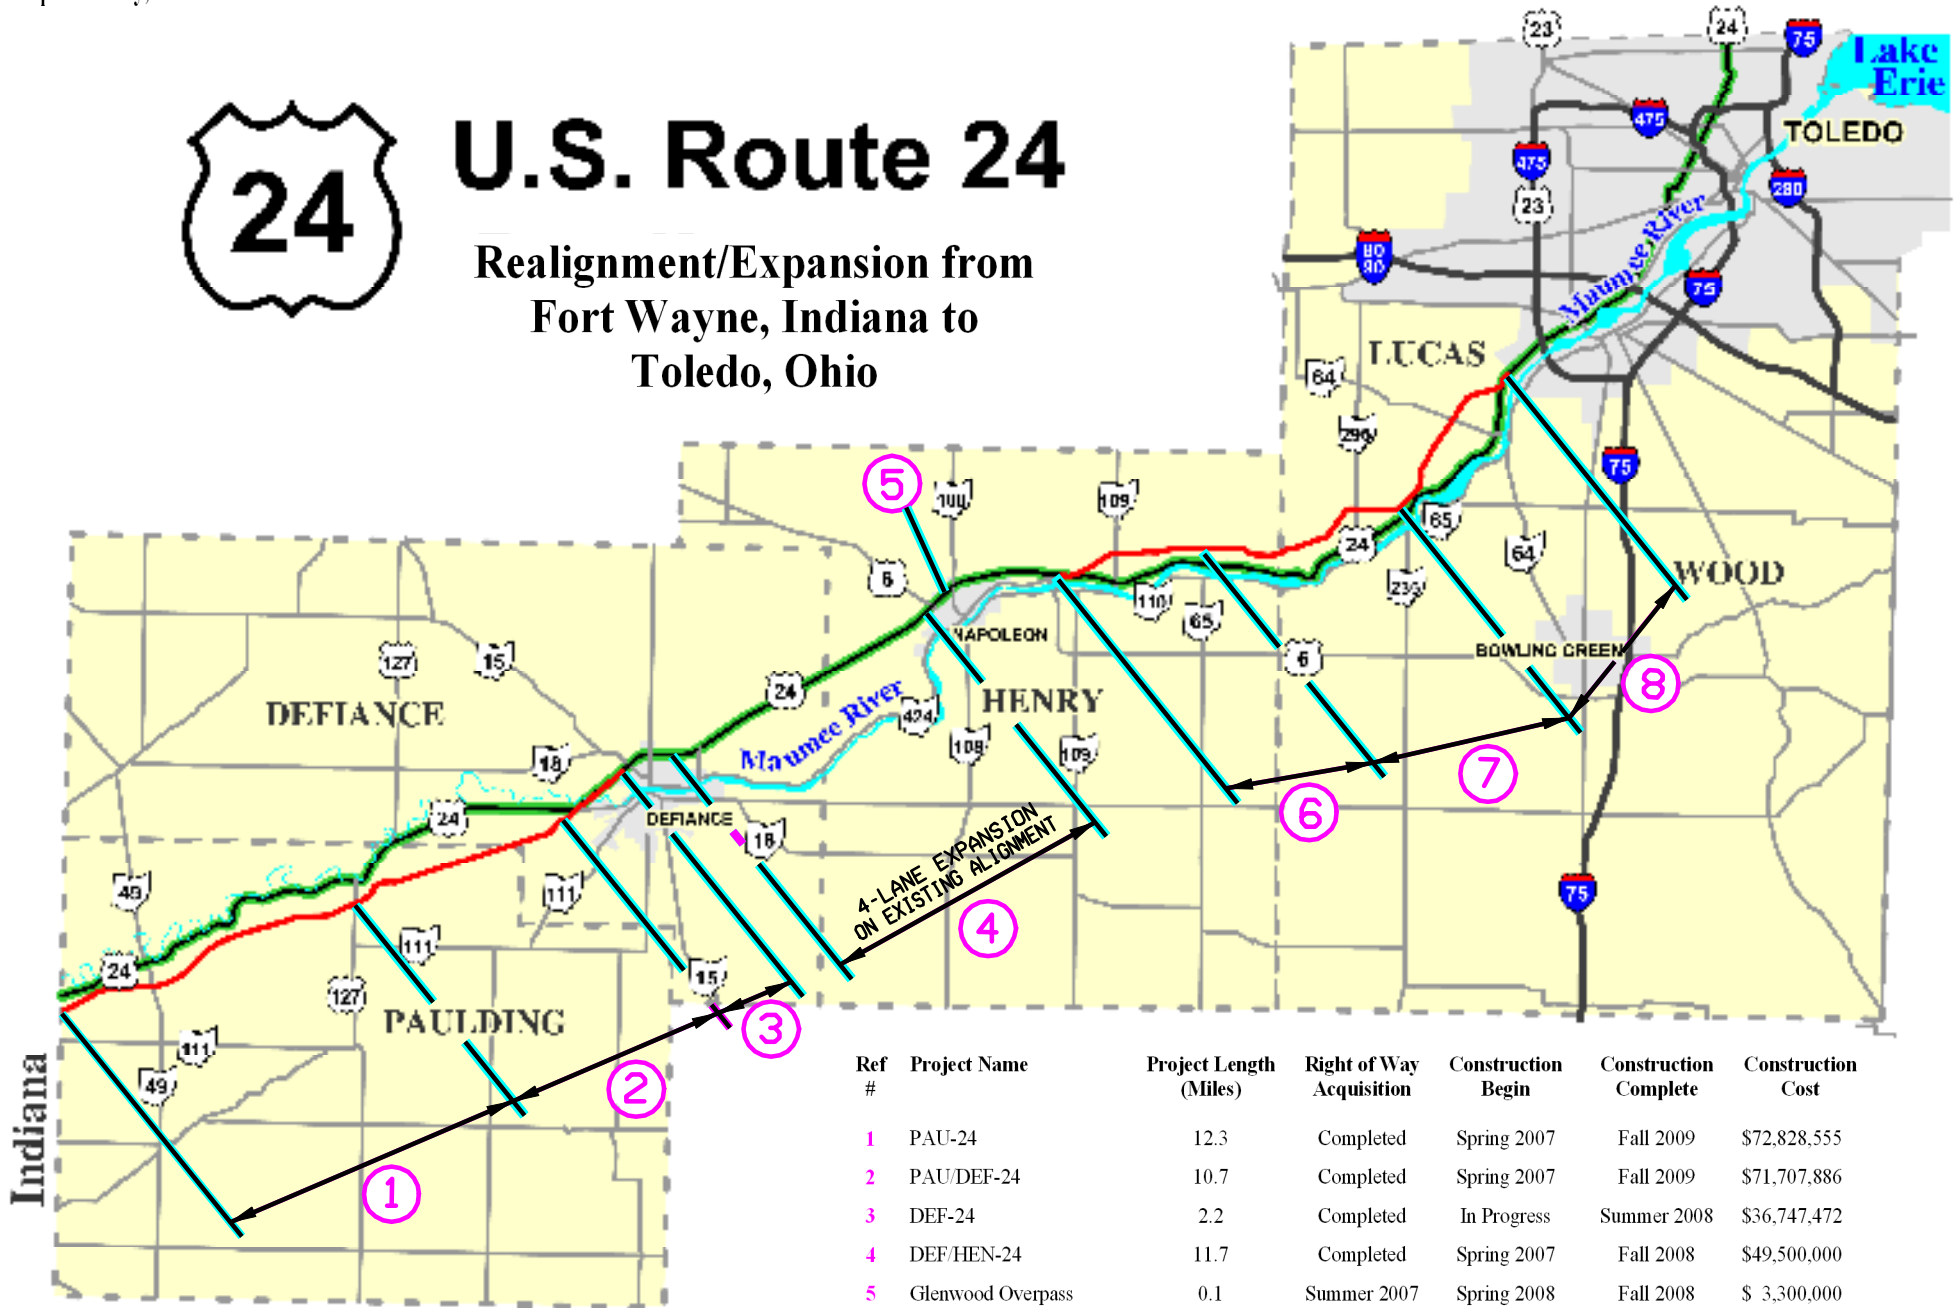

Ref #	Project Name	Project Length (Miles)	Right of Way Acquisition	Construction Begin	Construction Complete	Construction Cost
1	PAU-24	12.3	Completed	Spring 2007	Fall 2009	\$72,828,555
2	PAU/DEF-24	10.7	Completed	Spring 2007	Fall 2009	\$71,707,886
3	DEF-24	2.2	Completed	In Progress	Summer 2008	\$36,747,472
4	DEF/HEN-24	11.7	Completed	Spring 2007	Fall 2008	\$49,500,000
5	Glenwood Overpass	0.1	Summer 2007	Spring 2008	Fall 2008	\$ 3,300,000
6	HEN-24	5.2	In Progress	Spring 2008	Fall 2011	\$57,600,000
7	HEN/LUC-24	9.9	In Progress	Spring 2009	Fall 2011	\$70,200,000
8	LUC-24	6.5	In Progress	Spring 2009	Fall 2011	\$73,800,000

4-LANE EXPANSION ON EXISTING ALIGNMENT
